Daily Diary Report by Bid Item

Contract No.: **04-0120F4**
Diary #: **131** **Const Calendar Day:** 509 **Date:** **26-Oct-2013** **Saturday**
Inspector Name: **Gagnier, Pamela** **Title:** **Transportation Engineer**
Inspection Type: Continuous
Shift Hours: 07:00 AM 05:30 PM **Break:** **Over Time:**
Federal ID:
Location:
Reviewer: **Jefferson, Paul** **Approved Date:** 23-May-14 **Status:** Approved

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature **7 AM** **12 PM** **4PM**

Precipitation **Condition**

Working Day ☑ If no, explain:

Diary: Dispute ☐

E2 Shear Key Modifications

CCO 328 - HARRIS SALINAS
E2W East -
Finished mid layer horizontals, placed #19 rebars at saddle troughs (L rebars and angled). Installed PT tendons TL1, TL3 and TL 5. Also Layer B tie rebars.

CCO 329 - CONCO
E2W West -
Continue installing forms hardware and whalers.

CCO 327 - ABF
E2E East -
Today ABF crew installed SE lower saddle assembly. See M. Bruce diary for details.

I worked 10 hours overtime covering field activities.

CCO-328 **Bid Item:** **001** **0-BRS-ELS.328** **Pier E2 Bar Reinforcing Steel**

HARRIS SALINAS REBAR

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor:	HARRIS SALINAS REBAR							
Ironworker	JNM	ALFREDO CORPUS	0.00	8.00	0.00	8.00		☐
Ironworker	JNM	VILLASENOR GUELLERMO	0.00	8.00	0.00	8.00		☐
Ironworker	JNM	ZAVALA ALONZO	0.00	8.00	0.00	8.00		☐
Ironworker	JNM	WALTER GODOY	0.00	0.00	0.00	0.00		☐
Ironworker	JNM	DOUG WALLACH	0.00	0.00	0.00	0.00		☐
Ironworker	JNM	JUAN ROBLES	0.00	0.00	0.00	0.00		☐
Ironworker	JNM	DANIAL MONTES	0.00	8.00	0.00	8.00		☐
Ironworker	JNM	JAIME MONTES	0.00	0.00	0.00	0.00		☐
Ironworker	JNM	DANIAL GUDINO	0.00	8.00	0.00	8.00		☐
Ironworker	JNM	HECTOR LEON	0.00	8.00	0.00	8.00		☐
Ironworker	FOR	SIMON MARTINEZ	0.00	8.00	1.00	9.00		☐

CCO-329 **Bid Item:** **001** **0-PCC-ELS.329** **Pier E2 Place Concrete**

CONCO PUMPING

Labor

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Gagnier, Pamela **Diary #:** 131 **Date:** 26-Oct-2013 Saturday

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor:	CONCO PUMPING							
Carpenter	JNM	SALVADOR MARROQUIN	0.00	8.00	0.00	8.00		☐
Carpenter	JNM	PEDRO BARRON	0.00	8.00	0.00	8.00		☐
Carpenter	JNM	ABRAHAM RUELAS	0.00	8.00	0.50	8.50		☐
Carpenter	JNM	MIKE ABARRA	0.00	8.00	0.00	8.00		☐
Carpenter	JNM	SAL JIMENEZ	8.00	0.00	0.00	8.00		☐
Semi-Skilled Laborer	FOR	WENDELL STEPHENS	0.00	8.00	0.50	8.50		☐
Semi-Skilled Laborer	JNM	ARTURO SEGURA	0.00	8.00	0.00	8.00		☐
Carpenter	FOR	JAMES CROTTY	0.00	8.00	0.50	8.50		☐

Attachment

E2E East - ABF Installing South East Lower Saddle Assembly S4D

E2W East - HS Installing Top Longitudinal PT

E2W East - HS Installing Top Longitudinal PT

E2W East - PT Layer B Ties

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Gagnier, Pamela **Diary #:** 131 **Date:** 26-Oct-2013 **Saturday**

E2E East - ABF Installing South East Lower Saddle Assembly S4D

E2W West - Conco Installing Hardware and Whalers

E2W East - HS Installing Top Longitudinal PT

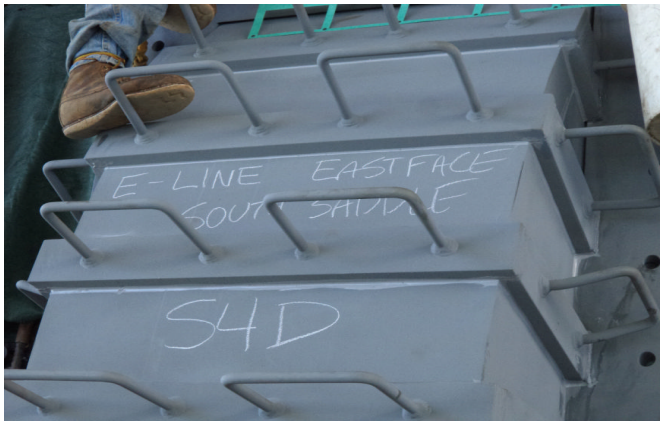

E2E East - ABF Installing South East Lower Saddle Assembly S4D

E2W West - Conco Installing Hardware and Whalers
