Daily Diary Report by Bid Item

Contract No.: 04-0120F4
Diary #: 132 **Const Calendar Day:** 510 **Date:** 27-Oct-2013 **Sunday**
Inspector Name: Gagnier, Pamela **Title:** Transportation Engineer
Inspection Type: Continuous
Shift Hours: 07:00 AM 05:30 PM **Break:** **Over Time:**
Federal ID:
Location:
Reviewer: Jefferson, Paul **Approved Date:** 23-May-14 **Status:** Approved

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature **7 AM** **12 PM** **4PM**

Precipitation **Condition**

Working Day ☑ If no, explain:

Diary: Dispute ☐

E2 Shear Key Modifications

CCO 328 - HARRIS SALINAS
E2W East -
Continue installing rebar at E2W east - Today they installed the outside horizontals, dead end PT bursting steel, PT duct for TL7 and TL8 and started on the vertical outside layer.
HS - southeast side of jacket wall ironworkers cut 2 #29 and 6 #25 horizontal rebars for the through cap tendon block outs installation and they replaced with 6 #29 and 7 #19 horizontal rebars. North east side of jacket wall ironworks cut 7 #25 and 1 #29 horizontal rebars for the through cap tendon block outs installation and they replaced with 6 #29 and 6 #19 horizontal rebars.

CCO 329 - CONCO
E2W West -
Continue installing hardwar and whalers.

CCO-328 **Bid Item:** **001** **0-BRS-ELS.328** **Pier E2 Bar Reinforcing Steel**
HARRIS SALINAS REBAR

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor:	HARRIS SALINAS REBAR							
Ironworker	JNM	ALFREDO CORPUS	0.00	0.00	8.00	8.00		☐
Ironworker	JNM	VILLASENOR GUELLERMO	0.00	0.00	8.00	8.00		☐
Ironworker	JNM	ZAVALA ALONZO	0.00	0.00	8.00	8.00		☐
Ironworker	JNM	WALTER GODOY	0.00	0.00	0.00	0.00		☐
Ironworker	JNM	DOUG WALLACH	0.00	0.00	0.00	0.00		☐
Ironworker	JNM	JUAN ROBLES	0.00	0.00	0.00	0.00		☐
Ironworker	JNM	DANIAL MONTES	0.00	0.00	8.00	8.00		☐
Ironworker	JNM	JAIME MONTES	0.00	0.00	0.00	0.00		☐
Ironworker	JNM	DANIAL GUDINO	0.00	0.00	8.00	8.00		☐
Ironworker	JNM	HECTOR LEON	0.00	0.00	8.00	8.00		☐
Ironworker	FOR	SIMON MARTINEZ	0.00	0.00	8.00	8.00		☐

CCO-329 **Bid Item:** **001** **0-PCC-ELS.329** **Pier E2 Place Concrete**
CONCO PUMPING

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor:	CONCO PUMPING							

Carpenter	JNM	ROBERT GARCIA	0.00	0.00	8.00	8.00	☐
Carpenter	JNM	ABRAHAM RUELAS	0.00	0.00	8.00	8.00	☐
Semi-Skilled Laborer	FOR	WENDELL STEPHENS	0.00	0.00	8.00	8.00	☐
Carpenter	JNM	JORGE GOMEZ	0.00	0.00	8.00	8.00	☐
Carpenter	FOR	JAMES CROTTY		0.00	8.00		☐
Carpenter	JNM	RALPH GOMEZ	0.00	0.00	8.00	8.00	☐

Attachment

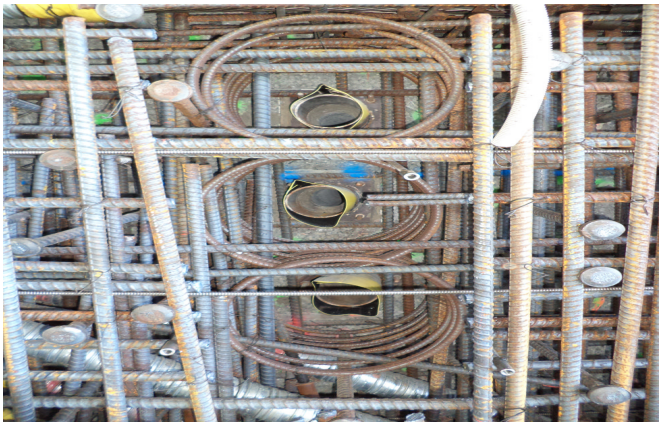

E2W East - Through Cap Tendon Blockouts shows replaced cut horizontal rebars

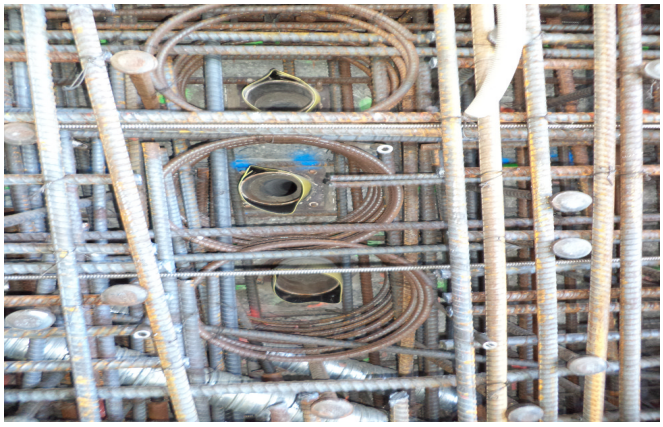

E2W East - Through Cap Tendon Blockouts shows replaced cut horizontal rebars

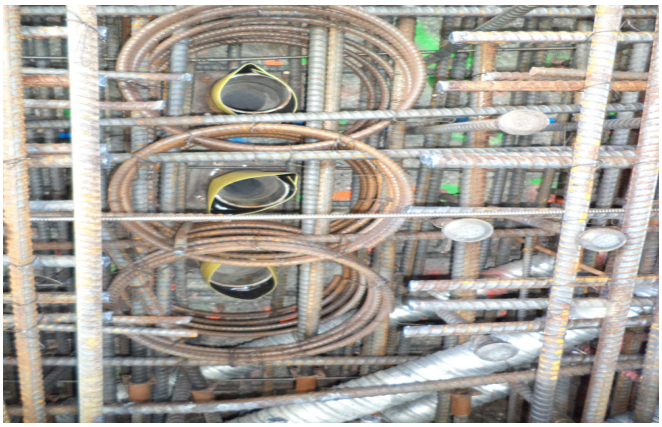

E2W East - Through Cap Tendon Blockouts shows replaced cut horizontal rebars
