Daily Diary Report by Bid Item

Contract No.: 04-0120F4
Diary #: 145 **Const Calendar Day:** 526 **Date:** 12-Nov-2013 Tuesday
Inspector Name: Gagnier, Pamela **Title:** Transportation Engineer
Inspection Type: Continuous
Shift Hours: 07:00 AM 05:30 PM **Break:** **Over Time:**
Federal ID:
Location:
Reviewer: Jefferson, Paul **Approved Date:** 23-May-14 **Status:** Approved

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature **7 AM** **12 PM** **4PM**

Precipitation **Condition**

Working Day ☑ If no, explain:

Diary: Dispute ☐

E2 Shear Key Modifications

CCO 328 - HARRIS SALINAS
E2E West - Today ironworkers placed draped tendon spirals and rest of horizontal rebars in the mid layer.

CCO 329 - CONCO
E2E East - Conco continues working on vertical form panels. In addition they are forming up at saddle troughs for grout pour.

CCO 330 - SDI
W-line - continue stressing tendons today they stressed tendons TL6-W, TL5-W, TL2-W TL1-W, TL7-W, TL8-W, TL4-E, TL3-E, TL6-E, TL5-E, TL2-E, TL1-E, TL7-E and TL8-E.

CCO-328 **Bid Item:** **001** **0-BRS-ELS.328** **Pier E2 Bar Reinforcing Steel**
HARRIS SALINAS REBAR

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: HARRIS SALINAS REBAR								
Ironworker	JNM	VILLASENOR GUELLERMO	8.00	2.00	0.00	10.00		☐
Ironworker	JNM	ZAVALA ALONZO	8.00	2.00	0.00	10.00		☐
Ironworker	JNM	WALTER GODOY	0.00	0.00	0.00	0.00		☐
Ironworker	JNM	DOUG WALLACH	0.00	0.00	0.00	0.00		☐
Ironworker	JNM	JUAN ROBLES	0.00	0.00	0.00	0.00		☐
Ironworker	JNM	DANIAL MONTES	8.00	2.00	0.00	10.00		☐
Ironworker	JNM	JAIME MONTES	8.00	2.00	0.00	10.00		☐
Ironworker	JNM	DANIAL GUDINO	8.00	2.00	0.00	10.00		☐
Ironworker	JNM	HECTOR LEON	8.00	2.00	0.00	10.00		☐
Ironworker	FOR	SIMON MARTINEZ	8.00	2.00	0.00	10.00		☐

CCO-329 **Bid Item:** **001** **0-PCC-ELS.329** **Pier E2 Place Concrete**
CONCO PUMPING

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: CONCO PUMPING								
Carpenter	JNM	JOSE REYES	8.00	0.00	0.00	8.00		☐
Semi-Skilled Laborer	JNM	PAT FINLEY	0.00	0.00	0.00	0.00		☐
Carpenter	FOR	JAMES CROTTY	8.00	0.00	0.00	8.00		☐

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Gagnier, Pamela **Diary #:** 145 **Date:** 12-Nov-2013 Tuesday

Carpenter	GEN	MARK WOZNICKI	8.00	0.00	0.00	8.00	☐
Carpenter	JNM	RICK PARKER	8.00	0.00	0.00	8.00	☐
Carpenter	JNM	SAL JIMENEZ	8.00	0.00	0.00	8.00	☐
Carpenter	JNM	ABRAHAM RUELAS	0.00	0.00	0.00	0.00	☐
Carpenter	JNM	RALPH GOMEZ	0.00	0.00	0.00	0.00	☐
Carpenter	JNM	PEDRO BARRON	8.00	0.00	0.00	8.00	☐
Carpenter	JNM	ROBERT CORTEZ	8.00	0.00	0.00	8.00	☐
Semi-Skilled Laborer	FOR	WENDELL STEPHENS	8.00	0.00	0.00	8.00	☐
Semi-Skilled Laborer	JNM	ARTURO SEGURA	8.00	0.00	0.00	8.00	☐
Carpenter	JNM	JOSE GIRON	8.00	0.00	0.00	8.00	☐
Carpenter	JNM	FELIPE CERVANTES	0.00	0.00	0.00	0.00	☐
Carpenter	JNM	SALVADOR MARROQUIN	0.00	0.00	0.00	0.00	☐
Carpenter	JNM	EFRAIN VILLAPANDO	0.00	0.00	0.00	0.00	☐
Carpenter	JNM	DANIEL GARCIA	8.00	0.00	0.00	8.00	☐
Carpenter	JNM	MIKE ABARRA	0.00	0.00	0.00	0.00	☐

Attachment

W-line stessing top longitudinal tendons

E2E - saddle trough with grout forms

W-line - elongation measurement

E2E West - Ironworkers installing rebar

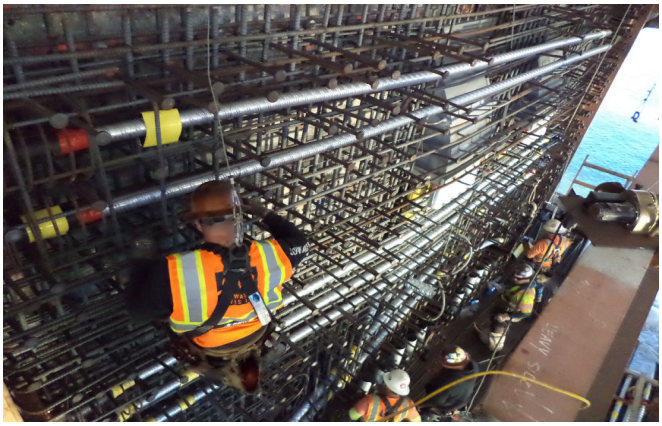

E2E West - Ironworkers installing rebar
