

State of California
 Business, Transportation and Housing Agency
 Department of Transportation

PROGRAM AMENDMENTS
 STIP Amendment 00S-014
 Notice Item
 CTC Meeting: March 28-29, 2001

Prepared By:
 Jim Nicholas
 Program Manager
 Transportation Programming
 (916) 654-4013

Agenda Item: 2.1b.(1)

Proposed

Original Signed By

 W. J. EVANS, Deputy Director
 Finance
 March 1, 2001

STIP AMENDMENT 00S-014 NOTICE

SUMMARY

This amendment delays a total of \$5,104,000 in Regional Improvement Program (RIP) funds programmed for construction on two local road projects in Tehama County, one on McCoy Road from FY 2001-02 to FY 2002-03 and the other on Flores Avenue from FY 2001-02 to FY 2003-04. There is no change in the total funding for the two projects.

RECOMMENDATION

The Tehama County Transportation Commission is requesting this amendment. The Department has reviewed the amendment and found it to be consistent with the Commission adopted STIP guidelines.

RESOLUTION

Resolved, that the California Transportation Commission (CTC) revise the 2000 State Transportation Improvement Program (STIP) at the end of the 30-day notice period as follows:

Revises:

Project Information								
County:	CT District:	PPNO:	EA:	Element:	Const Year:	PM Back	PM Ahead	Route/Corridor
Tehama	02	2162		LA	2001-02 2002-03			
Project Title:	McCoy Road Phase 3							
Sponsor:	Tehama County							
Implementing Agency:	Tehama County Public Works							
RTPA/CTC:	Tehama County Transportation Commission							
Location:	On McCoy Road north of the North Fork of Dibble Creek							
Description:	Realign Roadway (Phase 3)							

STIP Programming - RIP							(Dollars in Thousands)	
Component	PRIOR	2000/2001	2001/2002	2002/2003	2003/2004		Total	
PA&ED		\$25					\$25	
PS&E		\$30					\$30	
R/W		\$22					\$22	
CON			\$1,323	\$1,323			\$1,323	
TOTAL		\$77	\$1,323	\$1,323			\$1,400	

STIP Amendment 00S-014

March 28-29, 2001

STIP Programming - Total							(Dollars in Thousands)
Component	PRIOR	2000/2001	2001/2002	2002/2003	2003/2004		Total
PA&ED		\$25					\$25
PS&E		\$30					\$30
R/W		\$22					\$22
CON			\$1,323	\$1,323			\$1,323
TOTAL		\$77	\$1,323	\$1,323			\$1,400

And Revises:

Project Information								
County:	CT District:	PPNO:	EA:	Element:	Const Year:	PM Back	PM Ahead	Route/Corridor
Tehama	02	2032		LA	2001-02 2003-04			
Project Title:	Flores Avenue Access							
Sponsor:	Tehama County							
Implementing Agency:	Tehama County							
RTPA/CTC:	Tehama County Transportation Commission							
Location:	Near Proberta - Flores Avenue from Route 99 to Route 5							
Description:	Construct two-lane roadway							

STIP Programming - RIP							(Dollars in Thousands)
Component	PRIOR	2000/2001	2001/2002	2002/2003	2003/2004		Total
PA&ED							
PS&E							
R/W							
CON			\$3,655	\$3,655			\$3,655
TOTAL			\$3,655	\$3,655			\$3,655

STIP Programming - RIP (State Only to match TEA-21)							(Dollars in Thousands)
Component	PRIOR	2000/2001	2001/2002	2002/2003	2003/2004		Total
PA&ED	\$30						\$30
PS&E		\$93					\$93
R/W		\$37					\$37
CON			\$126	\$126			\$126
TOTAL	\$30	\$130	\$126		\$126		\$286

Local - TEA-21 (Proj # 0769)							(Dollars in Thousands)
Component	PRIOR	2000/2001	2001/2002	2002/2003	2003/2004		Total
PA&ED	\$120						\$120
PS&E		\$372					\$372
R/W		\$150					\$150
CON			\$502	\$502			\$502
TOTAL	\$120	\$522	\$502		\$502		\$1,144

STIP Programming - Total							(Dollars in Thousands)
Component	PRIOR	2000/2001	2001/2002	2002/2003	2003/2004		Total
PA&ED	\$150						\$150
PS&E		\$465					\$465
R/W		\$187					\$187
CON			\$4,283	\$4,283			\$4,283
TOTAL	\$150	\$652	\$4,283		\$4,283		\$5,085

BACKGROUND

This amendment delays a total of \$5,104,000 in Regional Improvement Program (RIP) funds programmed for construction on two local road projects in Tehama County. It delays \$1,323,000 programmed for construction from FY 2001-02 to FY 2002-03 for a roadway improvement project on McCoy Road and delays \$3,781,000 programmed for construction from FY 2001-02 to FY 2003-04 for a roadway construction project on Flores Avenue.

The McCoy Road roadway improvement project (PPNO 2162) is being delayed one year because additional realignment alternatives need to be considered. The original project schedule assumed that a Categorical Exemption would be the required environmental document under the California Environmental Quality Act (CEQA).

A Negative Declaration environmental document under CEQA is now required due to the additional realignment alternatives being considered. A Negative Declaration is a more detailed environmental document than a Categorical Exemption. The Negative Declaration is to be completed by August 2001 and the Environmental Assessment for the National Environmental Policy Act (NEPA) is scheduled for completion in December 2001. A time extension for allocation will be requested for the design (PS&E) and right of way components.


The Flores Avenue project (PPNO 2032) is being delayed two years because of additional environmental investigation required by the Department of Fish and Game. The environmental process requires that new winter studies be conducted to determine if a suspected threatened species is located within the project limits, and if not, then an extended study would be required through the spring and summer and possibly again next winter.

A time extension for allocation will be requested for the PS&E and R/W components, and an extension for expenditure for the Environmental component will be requested because of the newly required winter environmental study and the uncertainty of additional environmental studies needed.

ATTACHMENT

STIP AMENDMENT 00S-014

Location Map

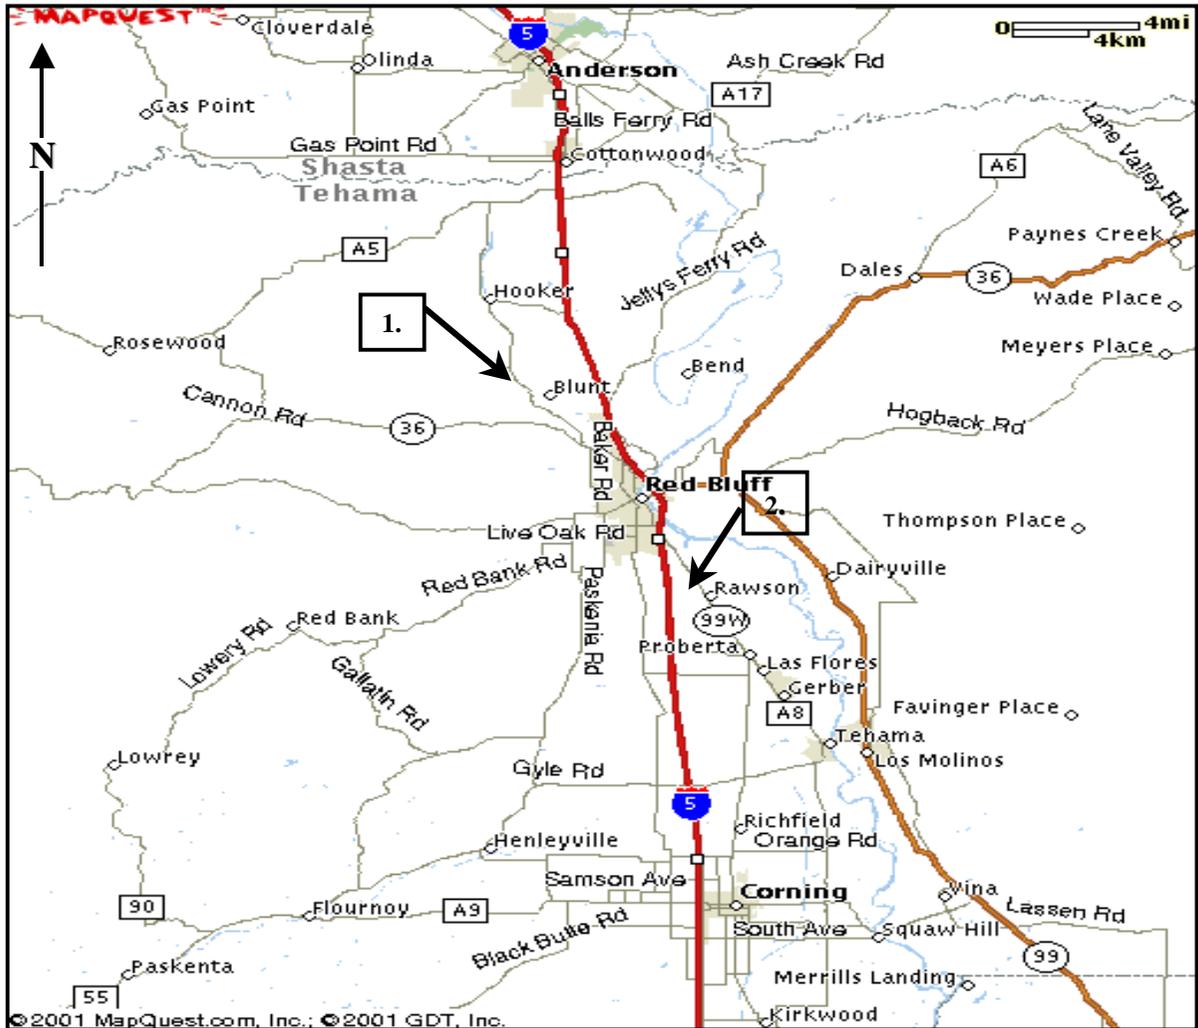

02-Tehama
PPNOS 2162 and 2032

- Location:
1. In Tehama County, McCoy Road near Dibble Creek
 2. Near Proberta, Flores Avenue
- Description:
1. Realign Roadway (Phase 3) and
 2. Construct two-lane roadway

