SECTION/SUBJECT

PAGE NUMBER

CHAPTER 2 ROLES AND RESPONSIBILITIES

CONTENTS

2.1 Introduction	2-1
STATE FUNDED PROJECTS	2-1
FEDERAL-AID PROJECTS	2-1
2.2 NATIONAL HIGHWAY SYSTEM	2-2
2.3 STEWARDSHIP AND OVERSIGHT AGREEMENT	2-2
2.4 DELEGATED PROJECTS	2-3
2.5 HIGH PROFILE PROJECTS	2-5
HIGH PROFILE PROJECT SELECTION PROCESS	2-5
2.6 RIGHT OF WAY CERTIFICATION DELEGATION	2-7
2.7 PROJECTS OFF THE NATIONAL HIGHWAY SYSTEM (NON-NHS)	2-7
2.8 PROJECTS ON THE NATIONAL HIGHWAY SYSTEM (NHS)	2-7
FIELD REVIEWS	
PS&E PROCEDURES FOR SIGNIFICANT NHS PROJECTS	
DESIGN STANDARDS	2-7
METHOD OF CONSTRUCTION	2-8
RESTRICTED CONSTRUCTION CONTRACT PROVISIONS	2-8
CONSTRUCTION ADMINISTRATION FOR SIGNIFICANT NHS PROJECTS	2-8
QUALITY ASSURANCE PROGRAMS	2-8
FINAL INSPECTION	2-8
2.9 FEDERAL-AID PROJECTS OF \$100 MILLION TO \$500 MILLION OR MORE	2-8
PROJECT MANAGEMENT PLAN	2-8
FINANCIAL PLAN	2-9
ASSISTANCE	2-9
2.10 FHWA RESPONSIBILITIES	2-11
PROJECT IMPLEMENTATION	2-11
2.11 CALTRANS RESPONSIBILITIES	2-12
POLICY AND PROCEDURES	
PROGRAM MANAGEMENT	2-12
PROJECT IMPLEMENTATION	
PROCESS REVIEWS	
MAINTENANCE REVIEWS	2-13

2.12 CITY, COUNTY AND OTHER LOCAL PUBLIC AGENCY RESPONSIBILITIES	2-13
PROJECT IMPLEMENTATION	2-14
2.13 CALIFORNIA TRANSPORTATION COMMISSION	2-15
Programming	2-15
FUND ALLOCATION	2-15
2.14 METROPOLITAN PLANNING ORGANIZATIONS, REGIONAL TRANSPORTATION PLANNI AND COUNTY TRANSPORTATION COMMISSIONS	
2.15 OTHER PUBLIC AGENCIES AND ORGANIZATIONS	2-15
2.16 REFERENCES	2-16
FIGURES	
FIGURE/DESCRIPTION	PAGE NUMBER
FIGURE 2-1: HIGH PROFILE/DELEGATED PROJECT IDENTIFICATION PROCESS	2-4
FIGURE 2-2: MAJOR FEDERAL-AID PROJECT FLOWCHART	2-10
Ехнівітѕ	
EXHIBIT/DESCRIPTION	PAGE NUMBER
EXHIBIT 2-A: CALTRANS DISTRICT LOCAL ASSISTANCE OFFICES	2-17
EXHIBIT 2-B: FEDERAL-AID PROJECT RESPONSIBILITIES LIST	2-19

CHAPTER 2 ROLES AND RESPONSIBILITIES

2.1 Introduction

Within Caltrans, the responsibility for administering and managing the federal and state local assistance highway programs resides in the Division of Local Assistance (DLA) under Planning and Modal Programs. Each of the twelve Caltrans districts has a District Local Assistance Engineer (DLAE) who is the local agency's primary contact for processing projects, providing assistance for local agency development efforts and answering local agency questions. Please refer to Exhibit 2-A "Caltrans District Local Assistance Offices," of this chapter for current district boundaries and mailing addresses.

The responsibility for implementing individual projects on the local streets, roads, and other transportation systems resides with the local agencies, principally the cities and counties.

STATE FUNDED PROJECTS

State funded local assistance projects must be developed in accordance with policy and procedural requirements as specified in state law, by the California Transportation Commission (CTC), and Caltrans. These state policies and procedural requirements are separate from federal requirements. It is Caltrans' policy to provide these funds to local transportation programs with a minimum of state oversight. However, because procedures vary with each state funding program the *Local Assistance Program Guidelines* (LAPG) should be referenced for a detailed explanation of the roles and responsibilities.

FEDERAL-AID PROJECTS

The Federal Highway Administration (FHWA) is the federal agency most typically involved in the transportation projects undertaken with federal funding and/or approval action for the programs discussed in this manual. It has the authority and responsibility for implementing and monitoring federal laws, regulations, and executive orders affecting these programs. When a project involves federal funding, the FHWA is involved according to these responsibilities and the delegations in the Stewardship Agreement described below. When another federal agency has permit jurisdiction or other role in the development of a project, the FHWA frequently becomes involved in the process as either lead or co-lead federal agency.

Caltrans obtained major delegations of authority and/or responsibility from FHWA as allowed under the provisions of the Safe, Accountable, Flexible, Efficient Transportation Equity Act: A Legacy for Users (SAFETEA-LU) of 2005 and previous Transportation Acts. Since the reengineering of local assistance procedures in 1995, Caltrans has passed on these delegations to local agency partners to the greatest extent possible. With each delegation goes the accountability for initiating and completing each project phase in accordance with the appropriate state, and federal laws and regulations without extensive FHWA, or State oversight. Caltrans has the responsibility to ensure that locals are administering the federal-aid program in conformance with the applicable federal requirements.

Federal-aid projects must be included in a regional transportation plan and the approved Federal Statewide Transportation Improvement Program (FSTIP). This inclusion must precede fund authorization for any activity for which federal-aid funds are being sought. The responsibility for selecting the program of projects for inclusion in the urbanized area Federal Transportation Improvement Program (FTIP) resides with the Metropolitan

Planning Organizations (MPOs). The County Transportation Commissions and Regional Transportation Planning Agencies (RTPAs) have also a role in programming projects for the FSTIP and the state funded State Transportation Improvement Program (STIP). Their selections must be done in consultation with the state, cities, counties, and other transportation agencies within the area. The FTIPs are incorporated into the FSTIP. Caltrans works with the non-MPO local agencies to program projects in the FSTIP.

Exhibit 2-B "Project Responsibilities List," outlines the roles and responsibilities of the parties involved in local federal-aid transportation projects. The chapters in this manual provide the details for carrying out these responsibilities.

2.2 NATIONAL HIGHWAY SYSTEM

ISTEA established provisions for Congress to adopt a National Highway System (NHS) to provide an interconnected system of principal arterials that serve major population centers, international border crossings, ports, airports, public transportation facilities, intermodal transportation facilities, other major travel destinations, meet national defense requirements, and serve interstate and interregional travel.

Until Congress made its official adoption, the NHS was defined as all principal arterials, including the Interstate System. On November 28, 1995, the President signed the legislation defining the NHS to include all Interstate routes, a selection of urban and rural principal arterials, the defense Strategic Highway Network including Strategic Highway Network Connectors and Intermodal Connectors. Currently there are about 160,000 NHS miles nationwide, including 7,655 NHS miles in California. Only about 324 of the 7,655 NHS miles in California are off the State Highway System (SHS).

See LAPG, Chapter 3, Federal-Aid Routes & Functional Classifications, for further discussion and a listing of the local agency NHS routes.

2.3 STEWARDSHIP AND OVERSIGHT AGREEMENT

The purpose of the FHWA/Caltrans Joint Stewardship and Oversight Agreement (Agreement) is to define roles and responsibilities, outline authorities, and assure accountability in effectively and efficiently managing program and project delivery of the Federal-Aid Highway Program (FAHP).

Authority for the Stewardship Agreement comes from 23 USC 106(c) which requires the United States Department of Transportation (USDOT) and the State to enter into an agreement for the extent to which the State assumes the project approval and oversight responsibilities of the USDOT.

Unlike previous Stewardship Agreements, the current Agreement utilizes a risk-based approach to manage the FAHP. This innovative way of doing business represents a paradigm shift in the joint and collaborative management of the FAHP. Through this Agreement, the FHWA has delegated responsibility for oversight and approval of low-risk project level activities to Caltrans.


The approach to high-risk project oversight is conducted in two steps as explained in Section 2.5: 1) select the projects that traditionally pose a risk to the health of the FAHP (High Profile projects), and 2) within each High Profile project, further delegate approval authorities for activities that pose a low risk to that individual project.

2.4 DELEGATED PROJECTS

Projects not selected as High Profile are lower-risk and referred to as "Delegated" projects. For Delegated projects, Caltrans has authority for all aspects of a Federal-aid project except those activities which may not be delegated by federal law (requiring FHWA approval). Prior to September 2007 these projects were referred to as "State-Authorized" projects defined by set criteria (rather than risk) such as non-Interstate 3R projects, Interstate construction projects under \$1 million, non-NHS projects, etc. Delegated projects include projects that are routine and inherently low risk in which Caltrans has a high level of experience and well documented procedures and processes in place for ensuring compliance with federal requirements. Project level approval authority for these projects follows that outlined in the Project Responsibilities List (Exhibit 2-B).

Over 99% of Local Assistance Projects are Delegated in which Caltrans or the local agency has approval authority for most project level activities. The FHWA's delegation of low risk project level approval to Caltrans only functions as long as those activities remain low risk. If oversight reveals concerns with Caltrans approval process for delegated activities, these activities have the potential to become high risk (High Profile), and therefore could alter Caltrans or the FHWA's involvement in their approval.

FIGURE 2-1: HIGH PROFILE/DELEGATED PROJECT IDENTIFICATION PROCESS

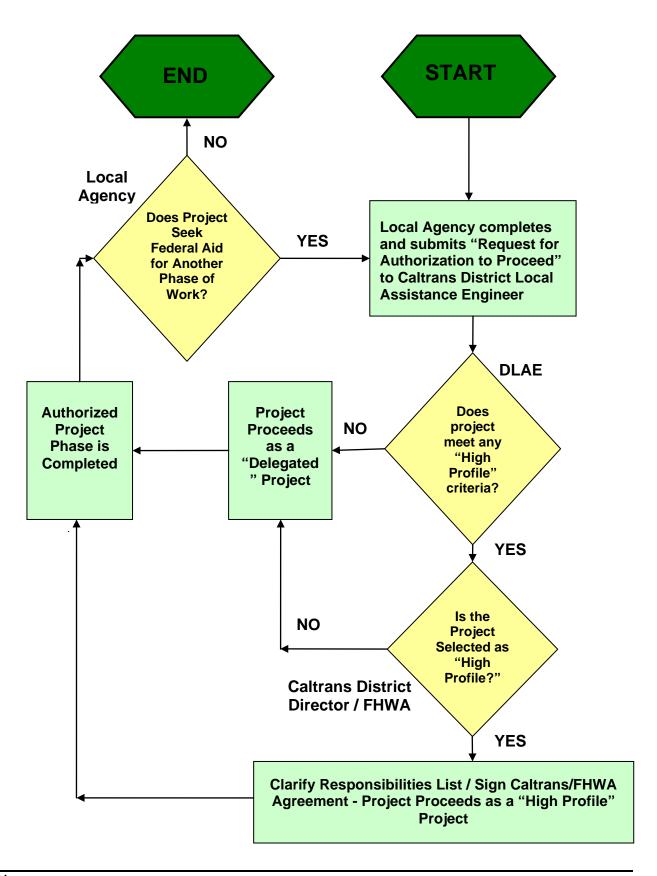

2.5 HIGH PROFILE PROJECTS

High-risk projects are designated as "High Profile" projects. Prior to September 2007 these projects were referred to as FHWA "Full-Oversight" projects based on set criteria (rather than risk) such as Interstate construction over \$1 million, major Intelligent Transportation System, etc. While Caltrans is responsible for approving most project level activities on low risk (Delegated) projects, the FHWA maintains many project level approval activities for High Profile projects.

Project level approval authority for "High Profile" project are project specific. Very few Local Assistance projects are designated as High Profile. Each High Profile project requires a unique Project Oversight Agreement, an example of which is shown in Appendix B of 2010 FHWA/Caltrans Joint Stewardship and Oversight Agreement.

HIGH PROFILE PROJECT SELECTION PROCESS

High Profile determinations are a joint, cooperative effort made on a project-by-project and phase-by-phase basis. Projects not meeting the criteria below are considered Delegated.

The criteria for High Profile project consideration are listed below. However, a project can meet one of these criteria but still not be determined by FHWA as High Profile.

- Controversial and Congressional Interest projects
- Pilot projects
- Executive Order 13274 projects Environmental Stewardship and Streamlining
- Interstate Projects containing:
 - o Design exceptions relating to the controlling criteria
 - o New or modified access points
 - o Innovative contracting method projects with Federal funds
- Invitational projects
- Major Intelligent Transportation Systems (ITS) projects
- Major Projects (>\$500 M)
- Non-Traditional Revenue Sources projects
- Special Experimental Projects Alternative Contracting (SEP-14)
- Special Experimental Projects Public Private Partnerships (SEP-15)
- Unusual Bridge and Structure projects

Caltrans and the FHWA jointly determine which projects are considered to be High Profile based on the criteria listed above. Appendix B of the FHWA/Caltrans <u>Joint Stewardship and Oversight Agreement</u> defines each criterion and provides examples. The High Profile project determination is made at the District level in conjunction with FHWA.

One goal under the Agreement is to identify High Profile projects and FHWA approval/involvement level as early as possible (prior to "Authorization to Proceed"). Continuous, open communication takes place throughout the year regarding the selection of High Profile projects. Quarterly meetings between Caltrans and the FHWA are scheduled to discuss any changes to the known or anticipated High Profile projects. Those projects selected as High Profile are mutually agreed upon by the appropriate Caltrans District and FHWA.

The steps for identifying High Profile Local Assistance projects are as follows (see Figure 2-1):

- 1. **Pre-Authorization:** Caltrans Local Assistance procedures, checklists, and forms required local agencies to assess proposed projects against the High Profile criteria and identify whether they think the project qualifies as a High Profile project prior to each "Authorization to Proceed".
- 2. *Initial Authorization to Proceed:* The local agency indicates whether the project meets any High Profile project criteria in their initial "Request for Authorization to Proceed" package (Exhibit 3-E of the Local Assistance Procedures Manual). The Caltrans District will assess the "Request for Authorization to Proceed" package to determine if the project meets any of the criteria for High Profile projects listed above. The District may request assistance from Caltrans Headquarters' Division of Local Assistance (DLA).

If the assessment reveals that the project does meet one or more of the above criteria, then the Caltrans DLAE will contact the FHWA Representative to discuss the assessment of the project. At this point, the Caltrans and FHWA representatives will jointly decide if the project meets the above criteria. If the joint decision is that one or more of the criteria are met, then the, representatives will jointly decide if the criteria met are enough to warrant selection as a High Profile project. If the project does not meet the criteria, as determined by the District Local Assistance Engineer (DLAE), then the project will move forward as a Delegated project.

Once a project has been selected as a High Profile project, a Project Oversight Agreement (refer to Appendix B of the 2010 Joint Stewardship and Oversight Agreement) will be filled out to identify FHWA and Caltrans project approval authorities for that particular project. The High Profile Project Agreement will document those areas where FHWA will have approval authority. It will also provide a project description, Federal-aid and State project numbers, and a discussion of FHWA's involvement on the project outside of the approval authority.

The DLAE will work directly with the Local Agency and FHWA to assure that the project responsibilities of the High Profile Project Agreement are fulfilled.

Caltrans headquarters' DLA may assist the District as requested. (For Major Projects, this information will be captured in an Oversight Agreement.) If a project is determined to be High Profile at the initial "Authorization to Proceed," then the High Profile Project Agreement will be revisited once the project moves closer to construction. The information within the High Profile project Agreement will be jointly agreed upon by the Caltrans District Director (or designee) and FHWA representatives and will include signatures acknowledging this Agreement. Appropriate local agency representative signature is optional.

3. Subsequent Authorization to Proceed: As in the initial "Request for Authorization to Proceed," the project will be reassessed against the High Profile project criteria by Caltrans DLAE and FHWA at each of the subsequent "Request for Authorization to Proceed" milestones. At these milestones, it will be jointly decided if the project meets the High Profile criteria and should be de-selected, selected, or continued as a High Profile project. If the reassessment at these milestones reveals that the project meets one of the High Profile criteria and should be selected as a High Profile project, then the same process described under step 2 of above will be followed. Otherwise, the project will proceed as a Delegated Project.

Once a project or phase is determined to be High Profile, the process is carried one step further by highlighting activities on the project responsibilities list that can be further delegated. The FHWA maintains approval authority for those activities that cannot, by law, be delegated and activities that may pose a risk to individual projects. Highlighted boxes in the "High Profile" projects column of the Project Responsibilities List (refer to Appendix B of the 2010 Joint Stewardship and Oversight Agreement) are designated as either the FHWA or Caltrans and signed and dated by both agencies. The documented and signed project responsibilities list may also include a general summary of other involvement, including attending regular meetings, conducting project inspections, etc.

2.6 RIGHT OF WAY CERTIFICATION DELEGATION

In addition to the delegations discussed above, the FHWA has also approved Caltrans request for delegation of right of way certificate approval for Delegated projects and not subject to FHWA oversight per the Stewardship Agreement. Procedures for processing local agency right of way certifications are described in Chapter 13, "Right of Way," of this manual.

2.7 PROJECTS OFF THE NATIONAL HIGHWAY SYSTEM (NON-NHS)

The reengineering of local assistance procedures in 1995 gave local agencies additional responsibility and accountability for non-NHS projects. Many of the responsibilities delegated to Caltrans under the Stewardship Agreement are further delegated to the local project sponsors. Caltrans preliminary engineering, construction review and approval activities are reduced, and other activities involving environmental reviews, project authorization, Disadvantaged Business Enterprises, consultant selection, and agreement procedures are streamlined to eliminate duplication of effort and multiple reviews.

2.8 PROJECTS ON THE NATIONAL HIGHWAY SYSTEM (NHS)

The delegation of responsibilities to local agencies described above for non-NHS projects also applies for NHS projects. With the following exceptions (discussed in detail in the appropriate chapters of this manual), procedures are the same for both types of projects.

FIELD REVIEWS

Field reviews are required for local agency projects on the National Highway System and encouraged for all other Federal-aid projects. If the field review is not performed, document on the field review form the reasons why the field review was not performed as a completed field review form is required for all Federal-aid projects.

PS&E PROCEDURES FOR SIGNIFICANT NHS PROJECTS

When Caltrans requires a field review for significant NHS projects, PS&E procedures (standards, agencies involved, use of consultants, project management, specifications, etc.) will be discussed. These procedures will be put in writing for Caltrans approval before final design is initiated. With approval, the local agency will then certify their PS&E(s) for these projects the same as they do for non-NHS projects upon completion of the PS&E. Caltrans may review the PS&E(s) if resources are available, or as part of a process review. NHS projects that are not "significant" will not require these approval procedures.

DESIGN STANDARDS

Local agencies are required to use only American Association of State Highways and Transportation Officials (AASHTO), 3R, and other design standards officially approved for use on NHS projects that are off the SHS. For SHS projects, Caltrans standards are to be used. Locally approved design standards are not allowed on NHS projects, however,

Caltrans may approve exceptions on a project-by-project basis except on High Profile projects, which requires FHWA approval.

METHOD OF CONSTRUCTION

In general, an open and competitive bidding process must be used for construction contracts on federal-aid projects. Exceptions to competitive bidding of construction contracts must be approved by Caltrans for "Delegated" projects. FHWA approval may also be required on High Profile projects.

RESTRICTED CONSTRUCTION CONTRACT PROVISIONS

Warranty clauses are restricted on NHS projects and the use of proprietary items is restricted on all federal-aid projects.

CONSTRUCTION ADMINISTRATION FOR SIGNIFICANT NHS PROJECTS

When Caltrans requires a field review for significant NHS projects, the local agency's construction administration procedures (staging, agencies involved, use of consultants, project management, quality assurance, etc.) will be discussed. These procedures will be put in writing for Caltrans approval before the "Request for Authorization for Construction" is approved. Caltrans will not review the construction administration unless requested and resources are available, or as part of a process review.

QUALITY ASSURANCE PROGRAMS

Local agencies shall use the Quality Assurance Program described in this manual for projects on or off the NHS. Caltrans will perform Independent Assurance (IA) if Caltrans test methods are used.

FINAL INSPECTION

The local agency will make a final inspection of completed "Delegated" projects prior to FHWA authorizing reimbursement of the final project voucher.

2.9 FEDERAL-AID PROJECTS OF \$100 MILLION TO \$500 MILLION OR MORE

PROJECTS OF \$500 MILLION OR MORE

The passage of "Safe, Accountable, Flexible, Efficient Transportation Equity Act: A Legacy for Users" (SAFETEA-LU) requires a local agency receiving any amount of federal financial assistance for a "major" project with an estimated total cost of \$500 million or more (includes all phases) and local agencies for such projects as may be identified by FHWA, submit to Caltrans for each project:

- A Project Management Plan
- An Annual Financial Plan

A cost Estimate Review must be completed by FHWA prior to the Final NEPA document, and prior to the construction authorization for all major projects (\geq \$500 million).

PROJECT MANAGEMENT PLAN

A draft Project Management Plan shall be submitted prior to the Record of Decision (ROD), Finding of No Significant Impact (FONSI), or Categorical Exclusion (CE) determination. A final Project Management Plan shall be submitted within 90 days after the ROD, FONSI, or CE determination which determine the scope of the projects. The plan shall:

- Document the procedures and processes that are in effect to provide timely and appropriate information to the project decision makers to effectively manage the scope, costs, schedules, quality of, and the federal and state requirements applicable to the project. Document the role of the agency leadership and management team in the delivery of the project
- Be updated and submitted prior to the authorization of federal financial assistance for construction and updated thereafter as required.

FINANCIAL PLAN

A Financial Plan for major projects of \$100 million to \$500 million or more shall:

- Be submitted when all elements of the plan are fully completed, but not later than when requesting authorization of federal financial assistance for construction. If the local agency waits until requesting authorization to submit the Financial Plan for projects \$500 million or more, the authorization will be delayed since FHWA HQ has to concur in the approval of the Financial Plan. For design build projects, the plan must be received prior to award of the design build contract.
- Be updated and submitted annually once the initial Financial Plan is approved until construction is substantially complete.
- Be based on detailed estimates of the cost to complete the project.
- Provide for the annual submission of updates to Caltrans that are based on reasonable assumptions as determined by Caltrans of future increases in the costs to complete the project.
- Use costs expressed in year of expenditure dollars and estimated using a riskbased approach consistent with current FHWA Cost Estimating Guidance located at:http://www.fhwa.dot.gov/ipd/project_delivery/defined/fhwa_delivery_process.htm

PROJECTS BETWEEN \$100 MILLION AND \$500 MILLION

SAFETEA-LU also requires that all local agencies receiving any amount of federal financial assistance for a project with an estimated total cost of \$100 million or more that is not covered by the above shall prepare an annual Financial Plan and make the plan available to Caltrans/FHWA upon request. FHWA-California Division has made a "blanket" request that Financial Plans for "major" projects with an estimated total cost of \$100 million or more, but less than \$500 million be submitted with the "Construction Authorization" request.

The process for submitting, reviewing, and approving these plans is shown in Figure 2-2. These projects require a "Project Oversight Agreement" (<u>Joint Stewardship Agreement</u>, <u>Appendix B</u>) signed by FHWA, Caltrans and, if applicable, the local agency.


ASSISTANCE

Information regarding the preparation, timing, etc., of the above plans is available through the DLAE. Other valuable information that may be helpful in the preparation of the above plans as well as other project areas is available at the FHWA Web site at:

http://www.fhwa.dot.gov/ipd/project_delivery/defined/fhwa_delivery_process.htm

FIGURE 2-2: MAJOR FEDERAL-AID PROJECT FLOWCHART

LOCAL AGENCY PROJECTS EQUAL OR OVER \$100 M (FP) & \$500 M (FP&PMP)

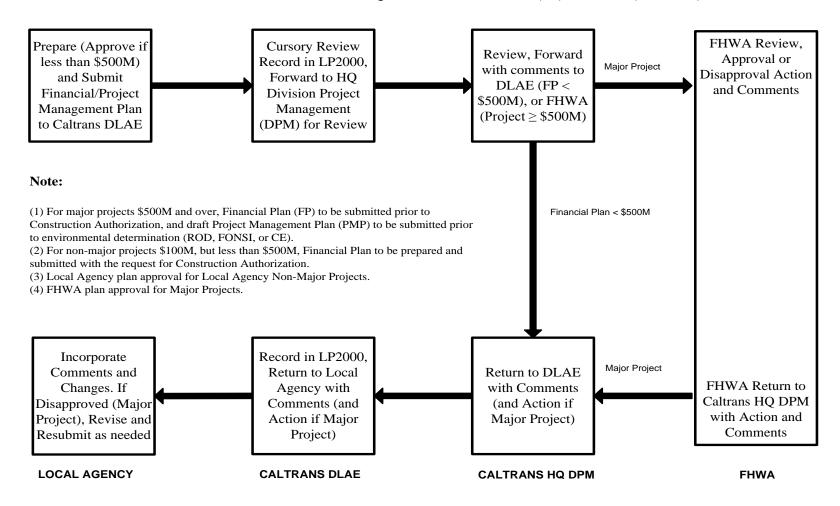

2.10 FHWA RESPONSIBILITIES

As discussed above, the FHWA has the overall responsibility for the Federal-Aid highway Program (FAHP) pursuant to 23 USC § 106 with the exception of the environmental responsibilities under SAFETEA-LU Sections 6004 and 6005 (23 USC § 326 and 327). In addition, the FHWA is ultimately responsible for ensuring the financial integrity and compliance with applicable federal laws and regulations.

Through the stewardship agreement, FHWA and Caltrans have committed to work cooperatively to identify appropriate stewardship and oversight initiatives using a risk-based, performance management approach. At the program level, strategic stewardship and oversight are to be achieved by effectively managing the program through: continuous program-level involvement; promoting new initiatives and concepts; participating on relevant joint task forces, joint committees, and joint quality improvement teams; assisting other stakeholders with program-related issues; conducting program assessments; conducting program reviews; and performance monitoring via performance measures and indicators.

PROJECT IMPLEMENTATION

At the project-level, strategic stewardship and oversight are accomplished through: conducting routine approval actions; verifying compliance through project-level samples; and conducting strategic project oversight. Routine approval actions are identified in Exhibit 2B and are those actions which have not been delegated to Caltrans. These include, but are not limited to:

- Federal-aid project agreements and modifications
- obligation of federal funds
- reimbursement to Caltrans of interim and final vouchers
- project-level conformity determinations
- right-of-Way Certificate 3
- protective buying and hardship acquisition
- new/modified interstate access determination of engineering and operations acceptability (minor access changes assigned to Caltrans, see letter dated September 15, 1994)
- design exceptions on the interstate
- Buy America waivers
- innovative contracting practices

Strategic project oversight is accomplished through the High Profile project process described in Section 2.5. For projects that are determined to be of high-risk to the FAHP, FHWA and Caltrans will jointly determine which project-level approvals will be retained by the FHWA Division office or delegated to Caltrans. In general, all major projects (those projects with total cost greater than \$500 Million) will be High Profile projects.

2.11 CALTRANS RESPONSIBILITIES

Caltrans is responsible and accountable to the FHWA for administering the successful implementation of federal-aid programs and projects in accordance with laws, regulations, and policies that govern the federal-aid program. Caltrans also administers the implementation of state funded programs and projects for the California Transportation Commission and State Legislature.

These responsibilities are divided into three areas: Policy and Procedures, Program Management, and Project Implementation.

POLICY AND PROCEDURES

Caltrans establishes uniform policies and procedures to assist the local agencies in meeting the program requirements for their projects. Caltrans in collaboration with FHWA interprets federal and state laws, rules and regulations, and provides guidance in the form of manuals, guidebooks, handbooks, reference materials and service, and training to assist the agencies in planning, designing, constructing, and maintaining their transportation systems.

Caltrans policy and procedure development is achieved in coordination and consultation with the FHWA, representatives of local agencies, MPOs, RTPAs, other affected agencies, and organizations.

PROGRAM MANAGEMENT

Each specific local assistance program provides funding which requires distribution, management, and oversight control to ensure that the funds are expended in accordance with the program requirements and that allocations and budget authority are not exceeded. Caltrans distributes both state and federal fund allocations to the MPOs, RTPAs, cities, counties and others as specified by law.

Once the distributions are established, Caltrans provides program guidance for their expenditure. Some programs may require annual or periodic project application and selection to establish eligibility lists. Caltrans also monitors project implementation to ensure that the projects are implemented in a timely manner to achieve program goals. The Local Assistance Program Guidelines describes each current program.

PROJECT IMPLEMENTATION

Some major federal-aid project implementation steps delegated by the FHWA to Caltrans cannot be further delegated to the local agency level and remain Caltrans' responsibility. These are shown in Exhibit 2-B and include:

- Funding Eligibility Determinations
- Acceptance of Right of Way certification and airspace agreement
- Railroad Agreement approval
- Utility Agreement and relocation approval
- Environmental approval actions pursuant to SAFETEA-LU Sections 6004 and 6005
- Financial Plans for projects over \$100 million
- Low Risk ITS project development
- Interstate access determination
- Some Public Interest Findings

- Approval of preliminary plans for major and unusual structures
- Design exceptions (for NHS)
- Value engineering (for NHS)
- Authorization of utility or railroad force account work
- Hiring of consultants in a management role
- Noise determination for PS&E approval
- Supplemental Work item justification
- Approval of liquidated damage rates
- Approval of major changes (requiring additional federal funds) and extra work
- ER damage assessments and report approval

The individual chapters covering these topics should be consulted for details concerning the responsibilities. Where the FHWA has not delegated final approval, Caltrans monitors local agency activities, reviews or prepares documents, and makes recommendations to FHWA.

Caltrans also provides assistance to the local agencies in interpreting the regulations, manuals and guidelines as they apply to specific project conditions. The District Local Assistance Offices and Headquarters DLA personnel are available to aid the local agency through the required process and procedural steps.

Where expertise is not otherwise available, the local agency may also request assistance from Caltrans technical specialists in solving special technical problems. Environmental issues, engineering services, right of way concerns, hazardous wastes, labor compliance, equal employment opportunity, Title VI, and Disadvantage Business Enterprise are among these areas where assistance is available. The use of this expertise must be requested early and be well coordinated to assure that Caltrans limited resources and personnel will be available when needed.

OVERSIGHT

As outlined in Chapter 19 "Oversight and Process Reviews," of the *Local Assistance Procedures Manual* (LAPM), Caltrans and FHWA will use the process review and other oversight methods to determine if local agencies are in compliance with all federal-aid laws, regulations, and procedures. The oversight findings will be used to evaluate all aspects (including Title 23 requirements) of the local agencies federal-aid program and to improve local assistance procedures.

MAINTENANCE REVIEWS

Annually, Caltrans reviews project maintenance for selected agencies using federal-aid funds so that every agency is covered during a four-year cycle. Chapter 18 "Maintenance," of the LAPM describes these maintenance review procedures in detail.

2.12 CITY, COUNTY AND OTHER LOCAL PUBLIC AGENCY RESPONSIBILITIES

The cities, counties, joint power authorities, transit agencies and other public agencies have the primary responsibility for implementing the specific projects which carry out the programs described in this manual. Nonprofit entities may also qualify for this. For the purpose of this manual, these agencies/entities are commonly called local agencies.

PROJECT IMPLEMENTATION

The local agency is responsible for the conception, planning, programming, environmental investigation, design, right of way, construction and maintenance of the projects on their local transportation system. It must ensure that its staff members, consultants and contractors comply with the applicable state and federal laws, regulations and procedures in developing, and constructing its projects.

If a local agency has never implemented a federal-aid or state funded project, or does so infrequently; it should review the processes with the DLAE prior to beginning any implementation activity. It may wish to seek the administrative services of another agency, which is more familiar with the process and procedure details.

Caltrans exercises its FHWA delegated authority by further delegating federal authority to local agencies to the greatest extent possible for those federal-aid projects that are located off of the State Highway System. The local agency is delegated decision-making authority and responsibility for most design and construction-related activities of federal-aid projects. These include:

- Getting the project into the FSTIP
- Preparing the Request for Authorization for each project phase
- Decision to hold field review for projects off the NHS
- Determining/Approving project DBE Availability Advisory percentage
- For ITS projects and other projects with ITS elements, make a preliminary classification of High-Risk, Low-Risk, or Exempt.
- Selecting consultant and approving consultant contracts
- Approving local design standards for projects off the NHS
- Approving design exceptions for projects "off" the NHS
- Preparing and Certifying PS&E (Caltrans must approve the local agencies' PS&E procedures for most NHS projects and FHWA for High Profile)
- Qualifying/selecting right of way consultants
- Right of Way acquisitions and relocation
- Preparing and approving Quality Assurance Programs (non-NHS projects only)
- Advertising and awarding construction project
- Construction contract administration and inspection (Caltrans must approve the local agencies construction administration procedures for high cost, complex, corridor-type NHS projects)
- Construction contract acceptance on delegated projects
- Coordinating railroad agreements
- Contract compliance

The individual chapters covering these topics should be consulted for details concerning the responsibilities.

2.13 CALIFORNIA TRANSPORTATION COMMISSION

The California Transportation Commission (CTC) has programming and fund allocation responsibility for some federal-aid and state funded programs used for local assistance projects. It is the responsibility of the local agency to notify the DLAE to request a CTC vote where applicable.

PROGRAMMING

The CTC currently selects federal Transportation Enhancements projects for inclusion in the STIP

FUND ALLOCATION

When a project is ready for implementation, the CTC must vote to allocate funding to the following programs. This action is commonly called the "**second vote**."

2.14 METROPOLITAN PLANNING ORGANIZATIONS, REGIONAL TRANSPORTATION PLANNING AGENCIES AND COUNTY TRANSPORTATION COMMISSIONS

These organizations have broad transportation planning duties and responsibility for programming most projects using federal-aid or state allocations from the programs described in this manual.

These organizations are responsible for providing each local agency with their application rules, procedures and timelines. They are also responsible for providing the local agency with results of the decisions about its projects and the agency, CTC and federal approval dates.

The local agency must work closely with these organizations to ensure that its projects are placed in the appropriate TIP with the correct funds in the proper years. Federal funds and many state funds cannot be obtained without this programming step.

Chapter 4 of the *Caltrans Project Development Procedures Manual* discusses the programming process in more detail.

2.15 OTHER PUBLIC AGENCIES AND ORGANIZATIONS

Other federal, state, regional and local entities may have an interest, role or jurisdiction in the development and implementation of a local project. Examples at the federal level include the Environmental Protection Agency, the Army Corps of Engineers, and the Fish and Wildlife Service. At the state level, examples include the Department of Fish and Game, Air Resources Board, and State Historic Preservation Officer, Regional agencies include the Air or Water Quality Control Boards and Flood Control Districts.

The State Resources Agency selects the projects to be funded by the CTC for the EEM program.

The role of these agencies will vary with the project scope, location and environmental impact. Coordination should begin early to prevent critical delays later in the project development.

Quasi-public or nonprofit organizations may apply for and receive programmed funds for some programs, notably EEM. These agencies must follow the same rules and regulations, which apply to any other local agency developing a state or federal-aid funded project. When such an agency does not have a full staff of administrative, engineering, contracting, or accounting personnel, Caltrans encourages it to work through a local agency that can provide these services and is familiar with the applicable rules.

2.16 REFERENCES

Joint Stewardship and Oversight Agreement: http://www.dot.ca.gov/hq/oppd/stewardship/


SAFETEA-LU Section 1904

23 USC 106(c)

FHWA Major Projects website:

http://www.fhwa.dot.gov/ipd/project_delivery/defined/fhwa_delivery_process.htm

EXHIBIT 2-A CALTRANS DISTRICT LOCAL ASSISTANCE OFFICES

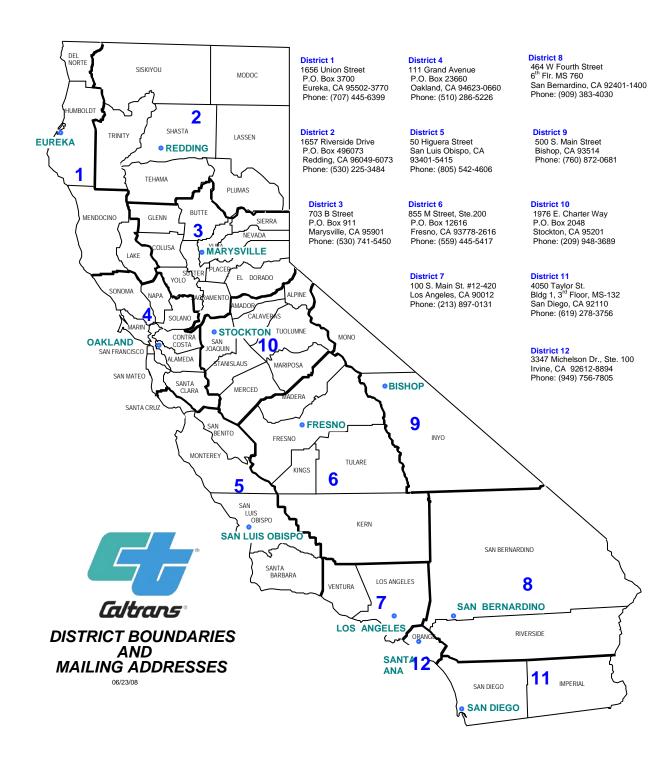

This page intentionally left bland

EXHIBIT 2-B: FEDERAL-AID PROJECT RESPONSIBILITIES LIST FOR DELEGATED PROJECTS OFF THE STATE HIGHWAY SYSTEM

(Pursuant to 2010 FHWA & Caltrans Joint Stewardship and Oversight Agreement)

Project Action/Activity	Local Agency	Caltrans District	Caltrans HQ	FHWA
Project Authorization (Chapter 3)				
Construction Engineering > 15% Total Contract Item Costs	Prepare	Approve	Review	Verify
Project Agreement and Modification [23 CFR 630.110]	Prepare	Recommend	Approve ²	Verify ³
Obligate Funds	-	-	-	Approve ⁴
Funding Eligibility Determinations	Prepare	Recommend	Approve	Verify⁵
Reimbursement Vouchers (interim and final)	-	-	Prepare	Approve
Section 1.9 Approvals of Incurred Costs. [23 CFR 1.9]	Prepare	Recommend	Recommend	Approve
Agreements (Chapter 4)				
Master Agreement	Sign	File Copy	Prepare/ Approve	-
Program Supplement Agreement	Sign	File Copy	Initiate/ Approve	-
Accounting/Invoices (Chapter 5)				
Invoice	Prepare	Approve ⁶	Approve ⁷	-
Project Eligibility	Prepare	Approve	Review	-
Environmental Procedures (Chapter 6)				
Project-Level Transportation Conformity Determination for CE pursuant to SAFETEA-LU 6005 MOU	Prepare	Request	-	Approve
NEPA Approval Consistent with SAFETEA-LU 6004 & 6005 MOUs (for detailed NEPA actions and approvals refer to LAPM Chapter 6 and the SER)	Prepare	Approve	-	-
Field Review (Chapter 7)				
Field Review	Perform	Participates ⁸	-	-
Minor ITS Project development [23 CFR 940.11] (SERF)	Prepare	Approve	-	-

² Approval and signatures are needed by both Caltrans and FHWA.

Page 2-19 June 10, 2011

³ Subject to FHWA's random sample verification process. Verification is defined as routine, independent confirmation of sampled projects.

⁴ Obligation of funds by FHWA is the final step in the project authorization process.

⁵ Subject to FHWA's random sample verification process.

⁶ Actions in italics such as "*Review*" indicate a change in procedures.

⁷ DLAE performs initial review and approval. Headquarters Local Programs Accounting performs final review of invoice prior to payment by the State which is subsequently reimbursed by FHWA.

⁸ DLAE participates in field reviews unless otherwise documented in project files.

Project Action/Activity	Local Agency	Caltrans District	Caltrans HQ	FHWA
Public Hearings (Chapter 8)				
Public Hearing [23 CFR 771.111(h)]	Perform & Certify	-	-	-
Civil Rights & Disadvantaged Business Enterprises (Chapter 9)				
DBE Implementation Agreement [LAPM]	Prepare	Approve	-	-
DBE Annual Goals [LAPM]	Prepare	Approve	-	-
ADA Coordinator [49 CFR 27.13(a)]	Certify	Accept	-	-
ADA Complaint Procedure [49 CFR 27.13(b)]	Certify	Accept	-	-
ADA Agency Self-Evaluation [28 CFR 35.105]	Certify	Accept	-	-
ADA Transition Plan [28 CFR 35.150]	Certify	Accept	-	-
Consultant Selection (Chapter 10)				
Consultant Selection [23 CFR 172.7-172.9]	Perform	Review ⁹	-	-
Consultant Agreements	Approve	Review ¹⁰	-	-
PIF – Use of Non-Competitive Negotiated Consultant Contracts [23 CFR 172.5(3)]	Prepare	Approve	-	-
Cognizant Agency Audit [23 CFR 172.7-172.9]	Prepare	Review ¹¹	-	-
Consultants in Management Role [23 CFR 172.9(d)]	Approve	Review ¹²	-	-
Design Standards (Chapter 11)				
Preliminary Plans for Major and Unusual Structures	Prepare	Approve	-	-
Design Standards	Approve	-	-	-
Design Exceptions, non-Interstate [23 CFR625.3]	Approve	-	-	-
Experimental Features	Prepare	Recommend	Recommend	Approve
Value Engineering [23 CFR 627, SAFETEA-LU 1904]	Approve	Review ¹³	-	-
Financial Plans for Projects from \$100 Million to \$499 Million [SAFETEA-LU 1904]	Prepare	Review & Approve	-	-
High Risk ITS Project Development [23 CFR 940.11]	Prepare	Recommend	Recommend	Approve

_

⁹ DLAE receives DBE information and may participate in consultant selection process upon request and contingent on available resources.

¹⁰ DLAE coordinates review of proposed consultant contract costs, etc. with Caltrans Audits & Investigations.

¹¹ DLAE coordinates review of proposed consultant contract indirect cost rates, etc. with Caltrans Audit & Investigations.

¹² DLAE reviews completed "Conflict of Interest for Consultants in Management Positions" form and the procedure used to hire consultant.

¹³ For all Federal-aid projects exceeding \$25 million on the National Highway System and bridge projects exceeding \$20 million on or off the Federal-aid system. DLAE to coordinate review of local agency Value Analysis Study with District Value Analysis Coordinator.

Project Action/Activity	Local Agency	Caltrans District	Caltrans HQ	FHWA
Major Projects and TIFIA Loan Projects – Project Management Plan and Financial Plan [SAFETEA-LU 1904]	Prepare	Review ¹⁴	Review	Approve
Low Risk ITS Project development [23 CFR 940.11]	Prepare	Approve	-	-
Plans, Specifications & Estimates (Chapter 12)				
PS&E [23 CFR 630.205, 23 USC 106]	Approve & Certify	Verify	-	-
Public Interest Finding (PIF) – Statewide Application	-	Recommend	Prepare	Approve
Environmental Commitments are incorporated	Prepare	Verify	-	-
PIF – Use of publicly furnished materials [23 CFR 635.407]	Approve	-	-	-
PIF –Use of proprietary products and processes [23 CFR 635.411]	Approve	-	-	-
PIF – Use of contracting method other than competitive Bidding [23 CFR 635.104/204]	Prepare	Approve	-	-
Utility or Railroad Force Account Work [23 CFR 645.113 & 646.216]	Approve	Verify	-	-
PIF – Advertising Period less than 3 Weeks [23 CFR 635.112]	Prepare	Approve	-	-
PIF – Use of Force Account [23 CFR 635.204,205]	Prepare	Approve ¹⁵	-	-
PIF – Use of Mandatory Borrow/Disposal Sites [23 CFR 635.407]	Approve	-	-	-
PIF – Use of Publicly-Owned Equipment [23 CFR 635.106]	Approve	-	-	-
Buy America Waiver [23 CFR 635.410]	Prepare	Recommend	Recommend	Approve
Innovative Contracting Requirements [SEP 14 & 15]	Prepare	Recommend	Recommend	Approve
Right-Of-Way (Chapter 13)				
Qualify Local Agencies	-	Approve	-	-
Qualify/Select Consultants	Perform/ Select	Verify	-	-
R/W certificate 3 – Conceptually concur as a condition of PS&E approval [23 CFR 635.309(r)(3)]	Prepare	Recommend	Recommend	Approve
Accept ROW certificate 1 and 2 as a condition of PS&E approval [23 CFR 635.309(c)(1)&(2)]	Prepare	Approve	-	-
Functional Replacement [23 CFR 710.509]	Prepare	Recommend	Recommend	Approve
Protective Buying and Hardship Acquisition [23 CFR 710.503]	Prepare	Recommend	Recommend	Approve
Public Interest Finding (PIF) – Concur on declaring Federally funded R/W as excess for disposal [23 CFR 710.403, 409]	Prepare	Recommend	Recommend	Approve
Railroad Agreement [23 CFR 646.216 (3)(d)]	Prepare	Approve		

DLAE to coordinate with Division of Project Management.
 Copy of approved force account PIFs to be forwarded to FHWA. For ARRA projects, force account PIFs are to be submitted to FHWA for approval.

Project Action/Activity	Local Agency	Caltrans District	Caltrans HQ	FHWA
Request for Credits for Early Acquisition of ROW [23 CFR 710.501]	Prepare	Recommend	Recommend	Approve
Request for Direct Federal Acquisition [23 CFR 710.603]	Prepare	Recommend	Recommend	Approve
Request for Federal Land Transfer [23 CFR 710.601]	Prepare	Recommend	Recommend	Approve
Request for Waivers of comparable replacement dwelling requirements [49 CFR 24.204(b)]	Prepare	Recommend	Recommend	Approve
Withholding of Federal Payments upon failure to perform [23 CFR 710.203(c), 23 CFR 1.36]	Prepare	Recommend	Recommend	Approve
Utilities Relocation (Chapter 14)				
Utility Agreement [23 CFR 645.113, 119]	Prepare	Approve	-	-
Utility Relocation [23 CFR 645 subparts A and B]	Prepare	Approve	-	-
Advertise & Award Project (Chapter 15)				
Advertise Project	Prepare	Recommend	Recommend	Approve ¹⁶
Bid Analysis [23 CFR 635.114]	Prepare & Approve	Review		
Consultant Agreements [23 CFR 172.7-172.9]	Approve	Review	-	-
Public Interest Finding (PIF) - Advertising Less than 3 Weeks [23 CFR 635.112]	Prepare	Approve	-	-
PIF - Use of Contracting Method other than Competitive Bidding [23 CFR 635.104 & 204]	Prepare	Approve	-	-
Advertisement Addendum [23 CFR 635.1129(c)]	Approve	-	-	-
Award of Project [23 CFR 635.114]	Approve	-	-	-
Rejection of All Bids [23 CFR 635.114]	Approve	-	-	-
Award Package – Including DBE Reporting	Prepare	Review	Report ¹⁷	-
Administer Construction Contract (Chapter 16)				
Construction engineering by local agency [23 CFR 635.105]	Certify	Approve	-	-
Contract Administration and Inspection	Certify	Review ¹⁸	Verify ¹⁹	Verify ²⁰
Subcontracting Requirements [23 CFR 635.114]	Certify	-	-	-
Quality Assurance Program [LAPM Chapter 16.14]	Approve	Accept	-	-
Contract Change Orders (CCO) w/no increase in Federal funds	Approve ²¹	-	-	

Approval for advertising is included with receipt of construction authorization for the project.

17 DBE data is reported to Caltrans Civil Rights.

18 DLAE may select areas for review.

19 DLA Oversight Engineers perform periodic reviews of contract administration for ARRA projects.

FHWA can verify any aspect of the project as part of a construction field review.
 Local agencies are financially responsible for change orders executed without additional e-76 funds.

Project Action/Activity	Local Agency	Caltrans District	Caltrans HQ	FHWA
E-76 Modification for CCO with increase in Federal funds	Prepare	Recommend	Approve	Approve ²²
Environmental Commitments (permit conditions and required mitigation) [23 CFR 771.109(b)]	Implement	-	-	-
Contract Time Extensions [23 CFR 635.120&121]	Approve	-	-	-
Termination of Construction Contract [23 CFR 635.125]	Approve ²³	-	-	-
Settlement of Construction Contract Claims [23 CFR 635.124]	Approve ²⁴	-	-	-
Incentive/Disincentive Amount Justification [23 CFR 635.127]	Approve	-	-	-
Liquidated Damages [23 CFR 635.127]	Approve	Review	-	-
Reimbursement Invoice	Prepare	Approve ²⁵	Approve	-
Project Completion (Chapter 17)				
Final Inspection/Contract Acceptance [23 USC 114(a)]	Approve	-	-	-
Materials Certification [LAPM Exhibit 17-G]	Certify	Review	Review ²⁶	
Project Verification	Recommend	Verify	-	-
Final Report of Expenditures	Prepare	Approve	-	Verify
Post-Project Audits	-	-	Perform ²⁷	-
Maintenance (Chapter 18)				
Maintenance of completed Federal-aid Projects	Perform	Review	-	-

²² Local agencies must receive e-76 modification approval prior to executing the CCO.

²³ Local agencies are financially responsible for termination agreements executed without necessary e-76 funds. Anticipated profits for work not performed is not eligible for Federal reimbursement.

Local agencies are financially responsible for settlement of contract claims without necessary e-76 funds. Any contract adjustment shall be fully supported.

²⁵ DLAE performs initial review and approval. Headquarters Local Programs Accounting performs final review of invoice prior to payment by the State which is subsequently reimbursed by FHWA. ²⁶ DLA Oversight Engineers perform periodic reviews.

²⁷ Performed by Caltrans Audits & Investigations with assistance from the DLAE.

is page intentionally left blat
