PROJECT DEVELOPMENT WORKFLOW TASK MANUAL

VERSION 2.0

Project Initiation Document

Lowest Appropriate WBS Level

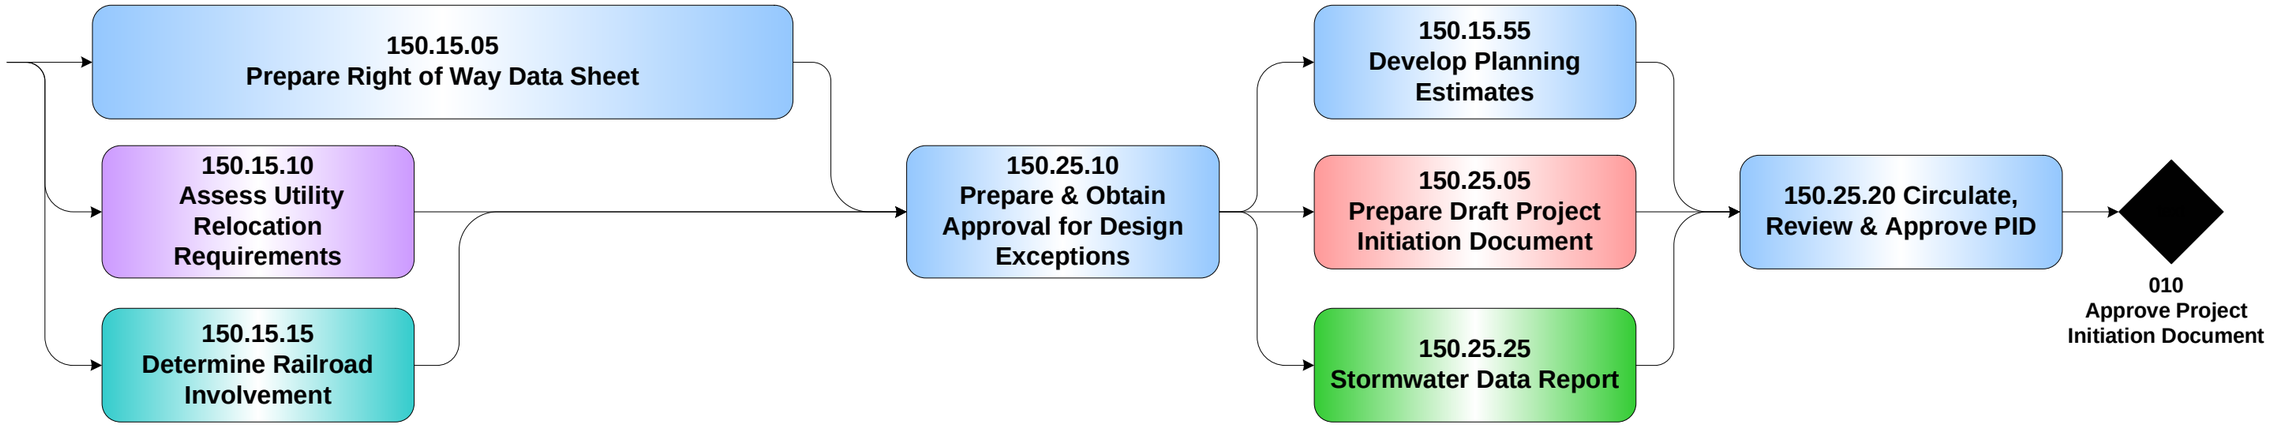

TASKS

P63	Prepare Preliminary R/W Estimate Map
P64	Request Right of Way Data Sheet Estimates
P65	Identify Preliminary Utility Relocation
P66	Request Right of Way to Assess Railroad Involvement
P67	Request Exception(s) and Approve Preliminary GAD
P68	Obtain FHWA Approval
P69	Submit DES Project Fact Sheet
P70	Obtain/Complete PSR-PDS Scoping Checklist
P71	Identify Mitigation Costs
P72	Prepare Project Cost Estimates
P73	Prepare Draft Project Initiation Document
P74	Prepare Risk Management Plan
P75	Prepare Attachments
P76	Prepare Storm Water Data Report
P77	Perform Draft PID Constuctability Review
P78	Prepare Functional Unit Project Fact Sheets
P79	Prepare Functional Unit(s) Workplan Estimate
P80	Identify and Estimate Consultant Effort
P81	Develop Consultant Contract Cost Estimate
P82	Incorporate Captal Outlay Support Estimate
P83	Circulate Draft PID for Internal Reviews
P84	Perform Task Force Field Review
P85	Circulate Draft PID for External Reviews
P86	Revise Draft PID
P87	Circulate PID for Signature
P88	Distribute Approved PID
P89	Complete Project Files
